



Vatika Infotech City Near GVK Toll Plaza Jaipur-Ajmer Expressway Thikaria, Jaipur 302 042 Rajasthan, INDIA

T 91.141.4067 101

Registered Office Vatika Limited Unit No A-002, INXT City Centre Ground Floor, Block A Sector 83, Vatika India Next Gurugram 122012, Haryana INDIA

T 91.124.4177 777 E info@vatikagroup.com

Date: 19.03.2024 vatika collections.com

To,

Chairperson,
Real Estate Regulatory Authority,
Rajasthan

Reference: Project "Vatika Infotech City for Part- A", Registration No. RAJ/P/2019/884

Subject: Regarding extra demand generated in Extension Application.

Honourable Ma'am,

The humble applicant would like to make this representation offline that Vatika Limited who had applied for the extension of project "Vatika Infotech City for Part- A" before the Honourable Authority on dated 11.12.2023 vide application no. **RAJ-RERA-APP-PE-2023-1196** and deposited statutory fee of Rs. 3,14,700 /- vides RERA-Trans-91 (on partial area i.e. 41959.74 sq mtr.)

Further, it is stated that humble applicant has obtained the partial completion certificate by the competent authority i.e. Chartered Engineer Nagendra Chaudhary on 20.09.2022 and the same partial completion certificate is uploaded on RERA web portal vide application no. RERA-PRD-2022-922 (30/11/2022) which was duly accepted by the authority on 09-03-2023.





Thereafter, the applicant completed the said project to the extent of 82.57% by 23.11.2023 and the same can be verified from the report of the chartered engineer dated 25.11.2023. The Jaipur Development Authority has issued the mortgage free letter dated 18.12.2023 vide letter no. जवीप्रा / उपा. / ज़ोन - 12/2023/ डी-9995 which substantiate the completion of the project upto 82.57%.

Thus, the extension application is presented only on partial area.

That order dated 17.03.2021 states that where promoter has completed partial part of the project and obtained partial completion certificate from local body/empaneled architect then the fee payable will be calculated only on the remaining portion of the phase area and if such remaining portion is less than 5000 square meters, then the fee payable will be calculated on 5000 square meters.

Thus, the applicant applied for further extension of the registration vides application no.RAJ-RERA-APP-PE-2023-1196 (11-12-2023). In the said application the Promoter applied for extension for part area i.e. 41959.74 sq mtrs as the remaining area was completed prior to the end date of the earlier extension.

Humble applicant wants to clarify that we have uploaded a hatched site plan showing the work completion of the project; two of block i.e. Block 1 and Block 3 (55.18%) are fully completed including their common facilities (Hatched in red and blue). Adding to it, Block 2 and Block 4 are partial completed including their common facilities also.



vatika® creating lasting value

(Hatched in green and yellow) against which local body has issued the mortgage free letter for 27.43 % more plot area, making it a total of 82.57%.

Further, by virtue of the same order which was referred while filing for the extension for the period 01-01-2023 to 31-12-2023 the promoter has applied for extension for part of the Project.

Adding to this, there are many precedents where the learned Authority has granted benefit of the said order to various promoter and to add to that the humble applicant was also allowed benefit of the said order in applied extension. Thus, the area 1,98,773.14 sq mtr. will be deducted from total land area for taking up the extension of the registration.

That the humble applicant request the kind Authority that the Promoter may kindly be allowed to file for extension for the part area and be allowed benefit of the order dated 17.03.2021.

The applicant requests the kind authority to consider our humble submission and relive us from depositing the extra fee.

Thanking you in anticipation.

Yours faithfully

For Vatika Limited

(Authorised Signatoryry)

View Notifications (7) 🌲



♣ Print (/Admin/PostApproval/PA\_SummaryPrint?ProjectId=1264&ApplicationID=922)



## Real Estate Project Detail

# PROJECT DETAILS

	AP	PLICATION NO. : R	ERA-PRD-2022-922 (30/11/2022)
Project Name	Vatika Infotech City for Part- A	Project Status	LAPSED
Registration No	RAJ/P/2019/884	Name of Promoter	VATIKA LIMITED

### PROJECT DETAILS APPLICATION NO.: RERA-PRD-2022-922 (30/11/2022) Project Address Khasra No./ Plot Project Type Plotted Development No.77, 78, 79, 80, 81, 90, 91, 92, 93, 85, 86, 87, 94, 95, 96, 97, 98, 99, 100, 106,119, 120, 121, 122, 20, 21, 101/1064, 103, 150/1066, 145/1065, 54, 139, 143, 144, 147, 148, 150, 151, 152, 153, 154, 155, 123, 55,61, 145, 146, 129, 134, 135, 136, 137, 138, 88, 89, 101, 102, 104, 105, 127, 173, 174/1256, 395,396,586/397,397, 187, 188, 189, 28/2, 532, 542, 543/1, 545, 532/1166, 546, 500/1239, 548/1, 548/2, 543, 501/1286, 540, 541, 538, 544, 548, 549, 1383/534, 533,13, 14, 15, 16, 17, 18, 19/1, Village-Thikaria, Prithvisinghpu ra, Sanjharia, Bagrukhu rd, Balmukundpura, Sanganer, Jaipur -302026 (Rajasthan) Estimated Finish 31-12-2021 Phase Area 240732.88 Date (in online form) 31-12-2023 ProjectLink Link of online summary Project registration vaild (../../Admin/Project/Summary? till (As per RC/ projectId=1264&type=1) Form F, whichever is

### PARTIAL COMPLETION CERTIFICATE

latest)

Name of Competent Authority/Empanelled Architect/Chartered Engineer who has issued the Partial Completion Certificate

PARTIAL COMPLETIO	ON CERTIFICATE
Date of issue of Partial Completion Certificate	20-09-2022
Block/Building/Tower for which partial CC issued	Block 1 and Block 3
Date of deposit of fee of partial CC with competent authority	20-09-2022
Date of deposit of a copy of partial CC (along with all requested documents) with the competent authority	20-09-2022
Upload Site plan/Layout plan highlighting the part for which partial CC is obtained (seal and signed by Competent Authority)	View (//Content/uploads/PA/Sitplan/22ccfa11-bc80-4614-88b3-a74899307eec.pdf)

PARA	Created BY	Comments	Date	Status	Document	
1	Rishabh Sharma (10665)	In the said case promoter has applied for the updation of the Partial Completion Certificate dated 20.09.2022 i.e., before the expiry of registration issued by Chartered Engineer Nagendra Chaudhary for the area 1,28,183.00 sq.mt. out of a total phase area of 2,40,732.88 sq.mt., the phase plan is attached in the application for reference, also peruse page no. 6 of the completion certificate in which Block 1 & 3 is 100% completed. Therefore, application is submitted for kind perusal and approval, please.	01- 12- 2022	PENDING WITH JOINT REGISTRAR		

#### Comments Details Created **PARA** Date Status Document BY Comments 2 Arpit CC may be accepted, submitted for 02-PENDING Sancheti kind perusal and further orders pls. 12-WITH (10683)2022 REGISTRAR 3 Submitted for perusal and decision, 02-Ramesh PENDING Sharma 12-WITH Sir. 2022 CHAIRMAN (9009)4 NIHAL Date of completion as per CC (if 07-**APPLICATION** CHAND different) filled as 15-09-2022 be 12-**OBJECTED** deleted. 2022 GOEL (1) 5 Promoter Dear Sir, we are unable to delete the 15-PENDING date "15-09-2022" from the tab "Date 12-WITH NODAL of completion as per CC (if different)". 2022 **OFFICER** So, we have written "20-09-2022" in the tab "Date of completion as per CC (if different)" which is same as Date of issue of Partial Completion Certificate. Kindly accept our humble submission and oblige us. User updated this details. Rishabh In reference to para 4/N, kindly peruse 6 18-PENDING Sharma the promoter reply at para 5/N. 02-WITH JOINT Submitted for kind perusal and further (10665)2023 REGISTRAR orders, please. 7 Arpit Promoter has filled the same date in 08-PENDING "Date of completion as per CC (if 03-Sancheti WITH (10683)different)" tab as "20-09-2022". 2023 REGISTRAR Therefore, submitted for kind perusal and approval.

Copyright © 2017 RAJ-RERA

Ramesh

Sharma

(9009)

NIHAL

CHAND

GOEL (1)

8

9

Developed & Maintained By RajCOMP Info Services Ltd. (http://risl.rajasthan.gov.in/)

08-

03-

09-

03-

2023

2023

PENDING

CHAIRMAN

Application

Approved

WITH

Approved

Submitted for perusal and decision, sir.

Project Name	Vatika Infotech City	for Part- A	Promote	er Name		VATIKA	A LIMITED	)
Project Registration No.	RAJ/P/2019/884		Project '	Туре		Plotted	DEVENUELEDEZ	
Estimated Finish Date (in online form)	stimated Finish Date (in online 31-12-2021		Project Registration Valid till (as per registration certificate)		31-12-2021 <u>View</u>		<u>v</u>	
Previous Extension Details of	Project							
Period of extension availed	f extension availed		Duration of extension				Form-F	
(From)	(To)	(	Months)		(Days)		Form	
01-01-2022	31-12-2022	1	2		0		<u> </u>	/iew
Project Extension Details								
Extension being Sought Upto				31-12-2	023			
Ouration of extension being sough	nt			12	Months		0	Days
Reason For Extension								
Other Than Force Majeure								
Explanatory Note regarding t	he stage of development	: works in the	project and	d reasons	for not comple	ting the c	levelopm	ent works
Explanatory Note regarding to the estimated finish date Explanatory Note is Uploaded.  andCost(as per online form)	he stage of development	works in the	project and	d reasons	for not comple	ting the c	levelopm	ent works
the estimated finish date		works in the	project and	d reasons	for not comple	ting the c	levelopm	ent work
che estimated finish date Explanatory Note is Uploaded.  andCost(as per online form) £ 21,33,37,000.00  Development Cost(as per onli £ 1,01,60,00,000.00	ne form)	works in the	project and	d reasons	for not comple	ting the c	levelopm	ent work
che estimated finish date Explanatory Note is Uploaded.  andCost(as per online form) £ 21,33,37,000.00  Development Cost(as per onli £ 1,01,60,00,000.00	ne form)	works in the	project and	d reasons	for not comple	ting the c	levelopm	ent works
che estimated finish date Explanatory Note is Uploaded.  andCost(as per online form)  21,33,37,000.00  Development Cost(as per onli  1,01,60,00,000.00  Form R1  Date of Latest Form R1(Certificate	ne form)	works in the	project and	d reasons	for not comple	ting the c	levelopm	
che estimated finish date Explanatory Note is Uploaded.  andCost(as per online form) £ 21,33,37,000.00  Development Cost(as per onli £ 1,01,60,00,000.00  Form R1  Date of Latest Form R1(Certificate  orm R2	ne form)  by Architect)  by Engineer)	works in the	project and	d reasons ₹ 24,00,0		ting the c		
che estimated finish date explanatory Note is Uploaded.  andCost(as per online form) f 21,33,37,000.00 Development Cost(as per onli f 1,01,60,00,000.00  form R1  late of Latest Form R1(Certificate form R2  late of Latest Form R2(Certificate stimated Construction Cost (Table	ne form)  by Architect)  by Engineer)  e A+B)	works in the	project and		0,000.00	ting the c		
che estimated finish date Explanatory Note is Uploaded.  andCost(as per online form) E 21,33,37,000.00 Development Cost(as per onli E 1,01,60,00,000.00  Form R1 Date of Latest Form R1(Certificate form R2 Date of Latest Form R2(Certificate estimated Construction Cost (Table cost Incurred on Construction (Tale	ne form)  by Architect)  by Engineer)  e A+B)	works in the	project and	₹ 24,00,0	0,000.00	ting the c		
che estimated finish date Explanatory Note is Uploaded.  andCost(as per online form) E 21,33,37,000.00 Development Cost(as per onli E 1,01,60,00,000.00  Form R1 Date of Latest Form R1(Certificate form R2 Date of Latest Form R2(Certificate	ne form)  by Architect)  by Engineer)  e A+B)  ble A+B)	works in the	project and	₹ 24,00,0	0,000.00	ting the c	No Docu	
che estimated finish date explanatory Note is Uploaded. andCost(as per online form) 21,33,37,000.00 Development Cost(as per onli 1,01,60,00,000.00  orm R1  ate of Latest Form R1(Certificate orm R2  ate of Latest Form R2(Certificate ostimated Construction Cost (Table ost Incurred on Construction (Tale orm R3  ate of Latest Form R3(Certificate	ne form)  by Architect)  by Engineer)  e A+B)  ble A+B)	works in the	project and	₹ 24,00,0 ₹ 14,70,0	0,000.00	ting the c	No Docu	ment
he estimated finish date explanatory Note is Uploaded. andCost(as per online form) 21,33,37,000.00 evelopment Cost(as per online form) 1,01,60,00,000.00  orm R1 ate of Latest Form R1(Certificate form R2 ate of Latest Form R2(Certificate form R1 cost Incurred on Construction (Table form R3 ate of Latest Form R3(Certificate form R3 ate of Latest Form R3(Certificate form R3 ate of Latest Form R3(Certificate form R3	ne form)  by Architect)  by Engineer)  e A+B)  ble A+B)	works in the	project and	₹ 24,00,0 ₹ 14,70,0	0,000.00	ting the c	No Docu	ment
che estimated finish date explanatory Note is Uploaded.  andCost(as per online form) £ 21,33,37,000.00 Development Cost(as per onli £ 1,01,60,00,000.00  form R1 Date of Latest Form R1(Certificate form R2 Date of Latest Form R2(Certificate estimated Construction Cost (Table cost Incurred on Construction (Tale form R3	ne form)  by Architect)  by Engineer)  e A+B)  ble A+B)  by Charted Accountant)	works in the	project and	₹ 24,00,0 ₹ 14,70,0 ₹ 21,	0,000.00 5,832.00 33,37,000.00	ting the c	No Docu	ment
che estimated finish date explanatory Note is Uploaded. andCost(as per online form) E 21,33,37,000.00 evelopment Cost(as per onli E 1,01,60,00,000.00  form R1  Pate of Latest Form R1(Certificate form R2  Pate of Latest Form R2(Certificate estimated Construction Cost (Table form R3  Pate of Latest Form R3(Certificate	ne form)  by Architect)  by Engineer)  e A+B)  ble A+B)  by Charted Accountant)	works in the	project and	₹ 24,00,0 ₹ 14,70,0 ₹ 21, ₹ 21, ₹ 24,	0,000.00 5,832.00 33,37,000.00 33,37,000.00	ting the c	No Docu	ment

Declaration cum Undertaking for Extension of Registration

I/ we do hereby solemnly declare and undertake:

That the project shall be completed by the extended project finish date, i.e., 31-12-2023 and that the desired extension (if granted) of registration

of the project shall not affect/ damage the rights and interests of the allottee(s) under the agreement for sale nor will it exonerate the promoter from his obligations to the allottee(s) under the Real Estate (Regulations and Development) Act, 2016 and rules & regulations made thereunder. If, however due to this extension, any damages or losses are suffered by any allottee(s), any rights and interests of any of the allottee(s) are affected or any dispute arises, promoter of the project shall be solely responsible and liable to compensate the same and to resolve the dispute and shall also be liable for all legal and financial consequence of delay in handing over the possession vis-à-vis what is previously agreed with the allottee(s).

#### Registered Phase Area

### Online Phase Area

240732.88

Payme	ent Details								
Actual PhaseArea Fees		Fees In (INR)	StandaradFees	ExtensionFees	PenaltyFees		Status		
240732	2.88		₹ 8,44,130.00	₹ 5,62,750.00	₹ 2,81,375.00	₹ 0.00		Paid	
Comm	ents Details								
PARA	Created BY	Comment	es .			Date	Status	Documen	
	Rishabh Sharma (10665)	Verify the	rify the fee deposited.				PENDING WITH DA/ ACCOUNTS/ LEGAL OFFICER/ LAW OFFICER		
2	Madan Pareek (16059)		O/- deposited by Rera 7 on corona pandemic ).	Frans. No. 408 dated 24.11.2	022 for extension of registration	28- 11- 2022	PENDING WITH NODAL OFFICER		
3	Rishabh Sharma (10665)		you ahve paid the ext fy on or before 05.12.2		instead of the complete phase	28- 11- 2022	APPLICATION OBJECTED		
4	Promoter	sq mtr, cor Block-3 adr the Partial PRD-2022- No. 2 and E extension f statutory fe	Promoter humbly submits to the kind authority that our project admeasuring 240732.88 ntr, consist of 4 blocks i.e. Block-1, Block-2, Block-3 and Block-4. Out of which Block-1 and k-3 admeasuring 128183 sq mtr has been completed and for the same we have uploaded Partial Completion Certificate under "Post Registration Tab" vide application no. RERA2022-922. Further, we want to apply for the extension of the remaining blocks i.e. Block 2 and Block no. 4 admeasuring 112549.89 sq mtr. Therefore we have applied for the insion for the remaining block i.e. block no. 1 and 3 and for the same we have paid the lutory fees of Rs 8,44,130/ Kindly accept our humble submission and oblige us. User lated this details.			30- 11- 2022	PENDING WITH NODAL OFFICER		
5	Rishabh Sharma (10665)		31-12-2023 w.r.t. the attached checklist.		01- 12- 2022	PENDING WITH JOINT REGISTRAR	<u>View</u>		
5	Arpit Sancheti (10683)	Submitted t	bmitted for kind perusal and further orders regarding extension pls.				PENDING WITH REGISTRAR		
7	Ramesh Sharma (9009)	Submitted f	Submitted for perusal and approval, Sir.				PENDING WITH CHAIRMAN		
3	NIHAL CHAND GOEL (1)	As the projection relevant.	s the project was registered in 2019, none of the reasons given for delay appear to be elevant.				APPLICATION OBJECTED		
	Promoter		ar Sir, we have uploaded the revised explanatory note for your kind perusal. Kindly accept r humble submission and oblige us. User updated this details.				PENDING WITH NODAL OFFICER		
0	Rishabh Sharma (10665)		n reference to para 8/N, promoter has uploaded the explanatory note in the Other occuments tab. Therefore, application is submitted for kind perusal and further order w.r.t.				PENDING WITH JOINT REGISTRAR		

	Sancheti (10683)	and further orders pls.	12- 2022	WITH REGISTRAR
12	Ramesh Sharma (9009)	Still explanatory not is vague and unsatisfactory, submitted for decision, sir	07- 12- 2022	PENDING WITH CHAIRMAN
13	NIHAL CHAND GOEL (1)	Approved	07- 12- 2022	Application Approved



## Er. Nagendra Chaudhary

B.E., F.I.E. (I), M.I.C.I., M.I.C.A., F.I.V., F.C.I.V., Chartered Engineer, Approved Valuer, Arbitrator, Surveyor & Loss Assessor.

Bill No.: NC/23-24/570

Date: 25.11.2023

## **Work Completion Certificate**

Name of Scheme

"Vatika Infotech City-Part A"

Village: Thikaria,

Prithvisinghpura uf Naiwala,

Sanjhariya, Bagru Khurd &

Balmukundpura urf Nada, Tehsil:

Sanganer, Ajmer Road, Jaipur

(Raj.)

Promoters & Devlopers

Address

M/s Vatika Ltd.



## **SUMMARY**

	~ CIVELLE REE	
A B	Total Area of Part-A (newly proposed layout) As per Approved Layout Plan, the Development Work has not been do	240732.89 sqm. one in highlighted
	portions.	
-1	Area of Block -1 (shown in map with red colour)	122768.00 sqm.
-2	Area of Block -2 (shown in map with yellow colour)	58125.00 sqm.
-3	Area of Block -3 (shown in map with Blue colour)	
-4	Area of Block -4 (shown in map with Green colour)	5415.00 sqm.
	Total $(1+2+3+4)$	54424.89 sqm.
		240732.89 sqm.
	Ratio of Block-1 in respect of Total Area of Part-A (1	
	*100/A)	51.00 %
	Ratio of Block-2 in respect of Total Area of Part-A (2 *100/A)	
	ga akti	24.15 %
	Ratio of Block-3 in respect of Total Area of Part-A (3 *100/A)	
		2.25 %
	Ratio of Block-4 in respect of Total Area of Part-A (4 *100/A)	22 (1.0/
		22.61 %
	Work done in Block-1	100.00 %
	Hence the percentage of work done in Block-1 in respect of Total Area	F1 00 0/
		51.00 %
	Work done in Block-2	78.20 %
]	Hence the percentage of work done in Block-2 in respect of Total Area	
,	n I ttal Al ca	18.88 %
	Work done in Block-3	100.00 %
F	Hence the percentage of work done in Block-3 in respect	
U	f Total Area	2.25 %
V	Vork done in Block-4	46.20 %
F	Ience the percentage of work done in Block-4 in respect	
0	f Total Area	10.44 %
S	o the Total percentage of work done in Part -A	
	newly proposed layout)	82.57 %
		02.57 70
	Magazida Chaudhawi Ell	
	Nagendra Chaudhary B.E., F.I.E. M.I.C.J., M.I.C.A.	
	M.I.C.I., M.I.C.A.	
	137	

### **DECLARATION**

This is to certify that work of the Township ""Vatika Infotech City-Part A" has partially been completed (as per detail enclosed) to the satisfaction as per policy of Urban Devlopment & Housing Deptt., Govt. of Rajasthan.

- a. The information furnished in part 1 is true and correct to the best of my knowledgeand belief.
- b. I have no direct or indirect interest in the scheme inspected.

c. I have personally inspected the scheme on dated: 23.11.2023

Date: 25.11.2023 Place: Jaipur


Signature of Chatered Engineer


F.I.V.







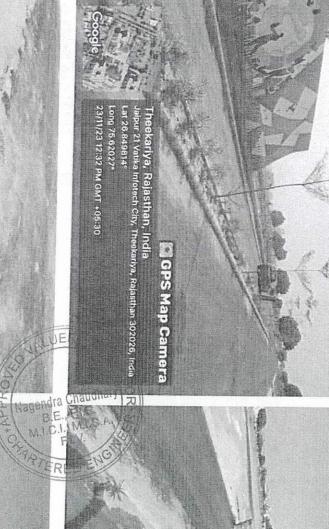

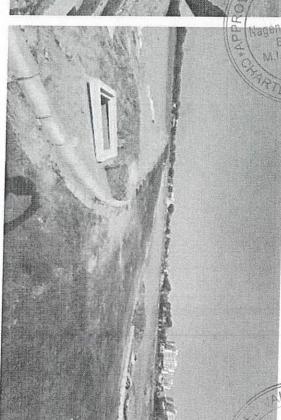



Nagendra Chaudhary O. B.E., F. F. M.I.C.I., M. P. F.I. T. P. T. P. F.I. T. P.



# जयपुर विकास प्राधिकरण, जयपुर

www.jda.urban.rajasthan.gov.in

क्रमांकःजविप्रा / उपा. / जोन-12 / 2022 / डी-3472-

ित्नांक 12-10-2022

मैसर्स वाटिका लि., मैसर्स वाटिका जयपुर सेज डवलपर्स लि. मैसर्स मेग्नेट डवलपर्स प्रा. लि.,मैसर्स नक्षत्र बिल्डकॉन प्रा. लि. जरिये अधिकृत हस्ताक्षरकर्ता श्री सुधीर शर्मा पुत्र श्री विनोद शर्मा, सुमन देवी पत्नी श्री काशीराम, एवं जीवनलाल पुत्र श्री रामदास, वाटिका इन्फोटेक सिटी, अजमेर रोड, ठिकरिया, जयपुर।

विषय:-

ग्राम ठिकरिया, पृथ्वीसिंहपुरा उर्फ नाईवाला, बगरू खुर्द, बालमुकुन्दपुरा उर्फ नाडा, सांझरिया एवं सीतापुराबास सांझरिया, तहसील सांगानेर अजमेर रोड, जयपुर में स्थित आवासीय योजना ''वाटिका इन्फोटेक सिटी'' पार्ट—ए में रहन रखे गये भूखण्डों को रहनमुक्त कर मानचित्र जारी करने बाबत।

उपरोक्त विषयान्तर्गत के कम में आप द्वारा प्रस्तुत ग्राम ठिकरिया, पृथ्वीसिंहपुरा उर्फ नाईवाला, बगरूखुर्द, बालमुकुन्दपुरा उर्फ नाडा, सांझरिया एवं सीतापुराबास सांझरिया, तहसील सांगानेर अजमेर रोड, जयपुर में स्थित आवासीय योजना "वाटिका इन्फोटेक सिटी" पार्ट—ए योजना के जिन मूखण्डों को जविप्रा में अनुमोदित योजना के 12.5 प्रतिशत क्षेत्रफल (15895.46 व.मी) के पेटे जविप्रा के पक्ष में रहन रखा गया है उन भूखण्डों का चार्टेड इंजीनियर द्वारा जारी अधिवास प्रमाण पत्र के आधार पर उक्तानुसार जयपुर विकास प्राधिकरण के पास रहन रखे गये क्षेत्रफल में से 8713.18 व.मी क्षेत्रफल को रहन मुक्त किया जाता है, जिसका अनुमोदित मानचित्र में अंकन कर मानचित्र की प्रति पत्र के साथ सलंग्न है।

सलंग्न :- उपरोक्तानुसार

AF

उपायुक्त जोन—12 जयपुर विकास प्राधिकरण, जयपुर उपायुक्त जोन-12 जयपुर विकास प्राधिकरण, अन्युर।



# जयपुर विकास प्राधिकरण, जयपुर

www.jda.urban.rajasthan.gov.in

क्रमांकःजविप्रा / उपा. / जोन-12 / 2023 / डी-999 5

दिनांक 18.12-2023

मैसर्स वाटिका लि., मैसर्स वाटिका जयपुर सेज डवलपर्स लि. मैसर्स मेग्नेट डवलपर्स प्रा. लि.,मैसर्स नक्षत्र बिल्डकॉन प्रा. लि. जिरये अधिकृत हस्ताक्षरकर्ता श्री सुधीर शर्मा पुत्र श्री विनोद शर्मा, सुमन देवी पत्नी श्री काशीराम, एवं जीवनलाल पुत्र श्री रामदास, वाटिका इन्फोटेक सिटी, अजमेर रोड, ठिकरिया, जयपुर।

> विषय :- ग्राम ठिकरिया, पृथ्वीसिंहपुरा उर्फ नाईवाला, बगरू खुर्द, बालमुकुन्दपुरा उर्फ नाडा, सांझरिया एवं सीतापुराबास सांझरिया, तहसील सांगानेर अजमेर रोड, जयपुर में स्थित आवासीय योजना "वाटिका इन्फोटेक सिटी" पार्ट-ए में रहन रखे गये भूखण्डों को रहनमुक्त कर मानचित्र जारी करने बाबत।


उपरोक्त विषयान्तर्गत के कम में आप द्वारा प्रस्तुत ग्राम ठिकरिया, पृथ्वीसिंहपुरा उर्फ नाईवाला, बगरूखुर्द, बालमुकुन्दपुरा उर्फ नाडा, सांझरिया एवं सीतापुराबास सांझरिया, तहसील सांगानेर अजमेर रोड, जयपुर में स्थित आवासीय योजना "वाटिका इन्फोटेक सिटी" पार्ट—ए योजना के जिन भूखण्डों को जविप्रा में अनुमोदित योजना के 12.5 प्रतिशत के पेटे क्षेत्रफल 15895.46 व.मी. रहन रखा गया था। जिसमें से पूर्व जविप्रा द्वारा क्षेत्रफल 8713.18 व.मी. के भूखण्ड रहन मुक्त किये जा चुके है।

अब वर्तमान में जयपुर विकास प्राधिकरण के पास रहन शेष क्षेत्रफल 7182.28 व.मी. में से चार्टेड इंजीनियर द्वारा जारी अधिवास प्रमाण पत्र के आधार पर क्षेत्रफल 4261.46 व.मी के भूखण्डों को रहन मुक्त किया जाता है, जिसका अनुमोदित मानचित्र में अंकन कर मानचित्र की प्रति पत्र के साथ सलंग्न है।

सलंग्न :- उपरोक्तानुसार

. उपायुक्त जोन–12 जयपुर विकास प्राधिकरण, जयपुर जयपुर

रामिकशोर व्यास भवन, इन्दिरा सर्किल, जवाहर लाल नेहरू मार्ग, जयपुर—302 004 दुरगाष — +91—141—2574798 : ईपीबीएक्स — +91—141—2569696 एक्सटे.: 8340 : फैक्स—1-91—141—2574555

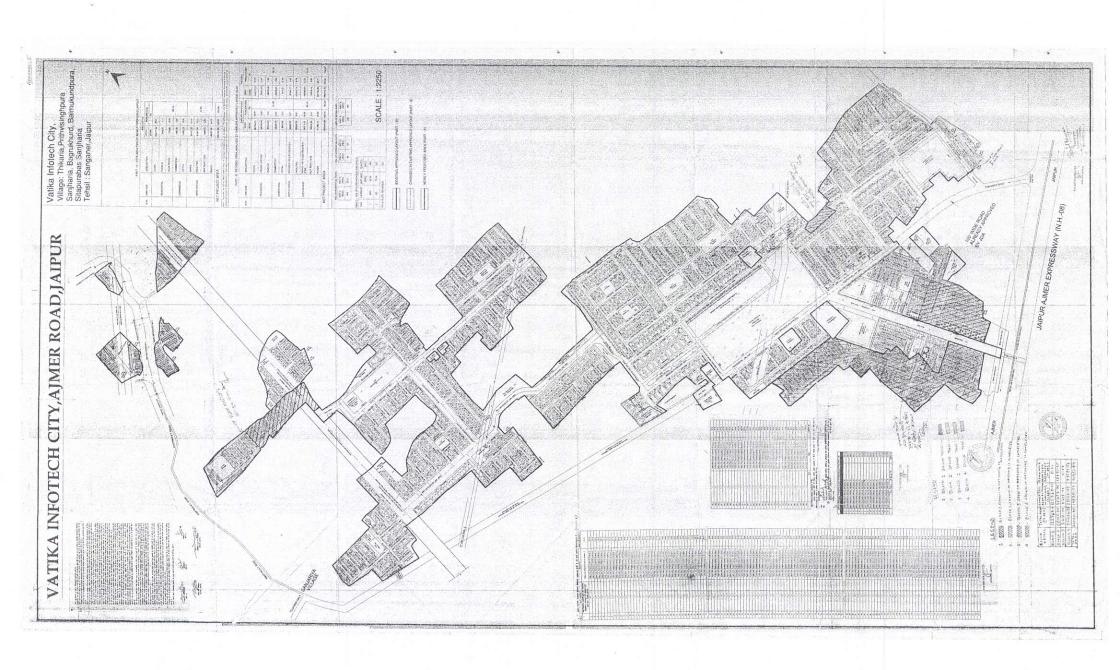



## राजस्थान रीयल एस्टेट रेग्युलेटरी ऑथोरिटी

द्वितीय एवं तृतीय तल, आरएसआईसी विंग, उधोग भवन, तिलक मार्ग, सी-स्कीम, जयपुर - 302005 फोन नं. – 0141–2851900 वेबसाईट & http://rera.rajasthan.gov.in

क्रमांक एफ.4(1)आरजे / रेरा / 2017 / पार्ट / 525 दिनांक :- 17 / 03 / 2021

### आदेश

दी रीयल एस्टेट (रेग्युलेशन एण्ड डवलपमेंट) एक्ट, 2016 की धारा 37 एवं दी राजस्थान रीयल एस्टेट रेग्युलेटरी ऑथोरिटी रेग्युलेशनस्, 2017 के अनुच्छेद 23(3) के अन्तर्गत ऑथोरिटी को प्रदत शक्तियों के क्रम में, निम्न निर्देश जारी किये जाते हैं:

आदेश क्रमांक 1429 दिनांक 25.08.2020 एवं आदेश क्रमांक 3080 दिनांक 16.08.2019 के पैरा 3 व 4 के अनुसार प्रोजेक्ट के पंजीकरण की वैद्यता अवधि बढ़ाने बाबत् देय फीस की गणना रजिस्ट्रर्ड प्रोजेक्ट के फेज ऐरिया के आधार पर की जाती रही है।

इस क्रम में ऑथोरिटी के समक्ष कतिपय ऐसे प्रकरण सामने आऐ हैं जिनमें रजिस्ट्रर्ड प्रोजेक्ट का फेज ऐरिया काफी बड़ा है एवं स्थानीय निकाय/एमपैनल्ड आर्किटेक्ट द्वारा आंशिक कम्पलीशन/ऑक्यूपेन्सी सर्टिफिकेट जारी किया जा चुका 高1

अतः अब भविष्य के लिये यह निर्धारित किया जाता है कि ऐसे प्रकरणों, जिनमें फेज ऐरिया 5000 वर्गमीटर से अधिक है एवं प्रोजेक्ट का आंशिक कम्पलीशन/ऑक्यूपेन्सी सर्टिफिकेट जारी हो चुका है, में फेज ऐरिया के जिस भाग का स्थानीय निकाय / एमपैनल्ड आर्किटेक्ट या अन्य अधिकृत प्रतिनिधि द्वारा आंशिक कम्प्रलीशन/ऑक्यूपेन्सी सर्टिफिकेट जारी किया जा चुका है को छोड़ कर फेज ऐरिया के केवल शेष भाग पर और यदि ऐसा शेष भाग 5000 वर्गमीटर से कम है तो 5000 वर्गमीटर पर देय फीस की गणना की जावेगी।

ऐसे प्रकरणों में प्रमोटर द्वारा Online extension application form के Actual Phase Area के कॉलम में, फेज ऐरिया के कम्पलीशन से शेष ऐरिया को भरा जाना होगा और यदि ऐसा शेष ऐरिया 5000 वर्गमीटर से कम है तो 5000 वर्गमीटर भरा जाएगा। साथ ही Online extension application form के Additional Information कॉलम में, यह सपष्ट करना होगा कि कितने ब्लॉक/भाग का

कम्पलीशन/ऑक्यूपेन्सी सर्टिफिकेट प्राप्त किया जा चुका है और उस भाग का ऐरिया कितना बनता है। इसके अतिरिक्त कम्पलीटेड ऐरिया और शेष ऐरिया को साईट प्लान/ले—आउट प्लान पर मार्क कर उसे व साथ ही प्राप्त सभी आंशिक कम्पलीशन/ऑक्यूपेन्सी सर्टिफिकेट को Online extension application form के Other documents tab में अपलोड करना होगा।

यह आदेश तुरंत प्रभाव से अर्थात् इसके जारी होने की दिनांक से लागू होगा और इसके आधार पर पूर्व में निर्णित किये जा चुके मामले पुनः नहीं खोले जायेगे।

यह आदेश ऑथोरिटी के अध्यक्ष महोदय के अनुमोदन से जारी किया जाता है।

Page 2 of 3

## प्रतिलिपि निम्न को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित है :-

- 1- PS to Chairman, Rajasthan RERA
- 2- PS to Member (Sh. Shailendra K. Agarwal), Rajasthan RERA
- 3- PS to Member (Sh. Salvinder Singh Sohata), Rajasthan RERA
- 4- PS to Adjudicating Officer, Rajasthan RERA
- 5- PS to Registrar, Rajasthan RERA
- 6- SA, DoIT & RISL Sh. Mukesh Arora
- 7- Coordinator, Conciliation Forum, Rajasthan RERA
- 8- Chairman/President, Confederation of Real Estate Developers' Associations of India (CREDAI) Rajasthan, 424, 4th Floor, Laxmi Complex, MI Road, Jaipur - 302001
- 9- Chairman/President, Confederation of Real Estate Developers' Associations of India (CREDAI) NCR Bhiwadi Neemrana, E-127, Industrial Area, Bhiwadi, Alwar-301019
- 10- President, Township Developer Association of Rajasthan (TODAR), Prim Pavilion, E-66, Nakul Path, Lal Kothi Scheme, Jaipur 302015
- 11- Chairman/President, Rajasthan Affordable Housing Developers Association (RAHDA) S-220, Time Square, Central Spine, Vidyadhar Nagar, Jaipur
- 12- Vice Chairman, RAJREDCO, Jaipur
- 13- Chairman, All India Federation of Tax Practitioners (CZ), c/o Shri Pankaj Ghiya, 10, Ganesh Colony, Bhairav Path, JLN Marg, Jaipur-302004
- 14- Chairman, RERA Awareness Committee, ICAI, Jaipur Branch, Jain Rathore & Associates, 105, Jagdish Enclave, Hawa Sadak, Civil Line Circle, Opp. Ram Mandir, Jaipur-302006.
- 15- Chairman, RERA Committee, Tax Consultant Association, Jaipur, 801-803, 8th Floor, Signature Tower, DC-2, Behind Apex Bank, Tonk Road, Jaipur – 302015
- 16- President, RERA India Educational & Resources Federation, 4F-42, Mahima Triniti Mall, Swage Farm, New Sanganer Road, Jaipur-302019
- 17- Chairman, The Indian Institute of Architects, Rajasthan Chapter, 400, F-72, 'Suryoday', Subhash Marg, Bagadiya Bhawan, C-Scheme, Jaipur-302001
- 18- Chairman/Secretary, Rajasthan Realtors Association (RRA), 308, 3<sup>rd</sup> Floor, Plot No. 1, Felicity Tower, Sahakar Marg, Lal Kothi, Jaipur- 302005
- 19- Chief Editor, RERA Times, Ghiya & Company, E-68, Ghiya Hospital Complex, Sector-12, Malviya Nagar, Jaipur – 302017
- 20- All officers of Rajasthan RERA
- 21- Guard File
- 22- Rajasthan RERA Website
- 23- All promoters (through their dashboard)

स्जिस्ट्रार
