


Ashiana Nitara, PH-2

Phase Start Date = 01 April 2025

Sr.No	Description	Start Date	Duration	Finish Date
1	Foundation	02-Jul-25	91	01-Oct-25
2	RCC super structure	02-Oct-25	303	01-Aug-26
3	Brick Work	03-Jan-26	302	01-Nov-26
4	Internal Plaster	04-Mar-26	303	01-Jan-27
5	Tiles Work	03-May-26	302	01-Mar-27
6	External Plaster	08-May-26	300	04-Mar-27
7	POP Work	07-Jul-26	300	03-May-27
8	Door Shutter Fixing	07-Aug-26	300	03-Jun-27
9	Aluminium Window	05-Sep-26	300	02-Jul-27
10	Electrical wiring & Fittings and testing	30-Oct-26	305	31-Aug-27
11	Internal Painting	29-Nov-26	300	25-Sep-27
12	CP & Vitreous Fittings	04-Mar-27	375	13-Mar-28
13	External Painting	28-Jan-27	300	24-Nov-27
14	Fire Fighting	20-Oct-26	240	17-Jun-27
15	Lift	29-Nov-26	300	25-Sep-27
16	Solar	18-May-27	250	23-Jan-28
17	Obtaining Completion Certificate	13-Mar-28	45	27-Apr-28
18	Final finishing and hand over	27-Apr-28	181	25-Oct-28

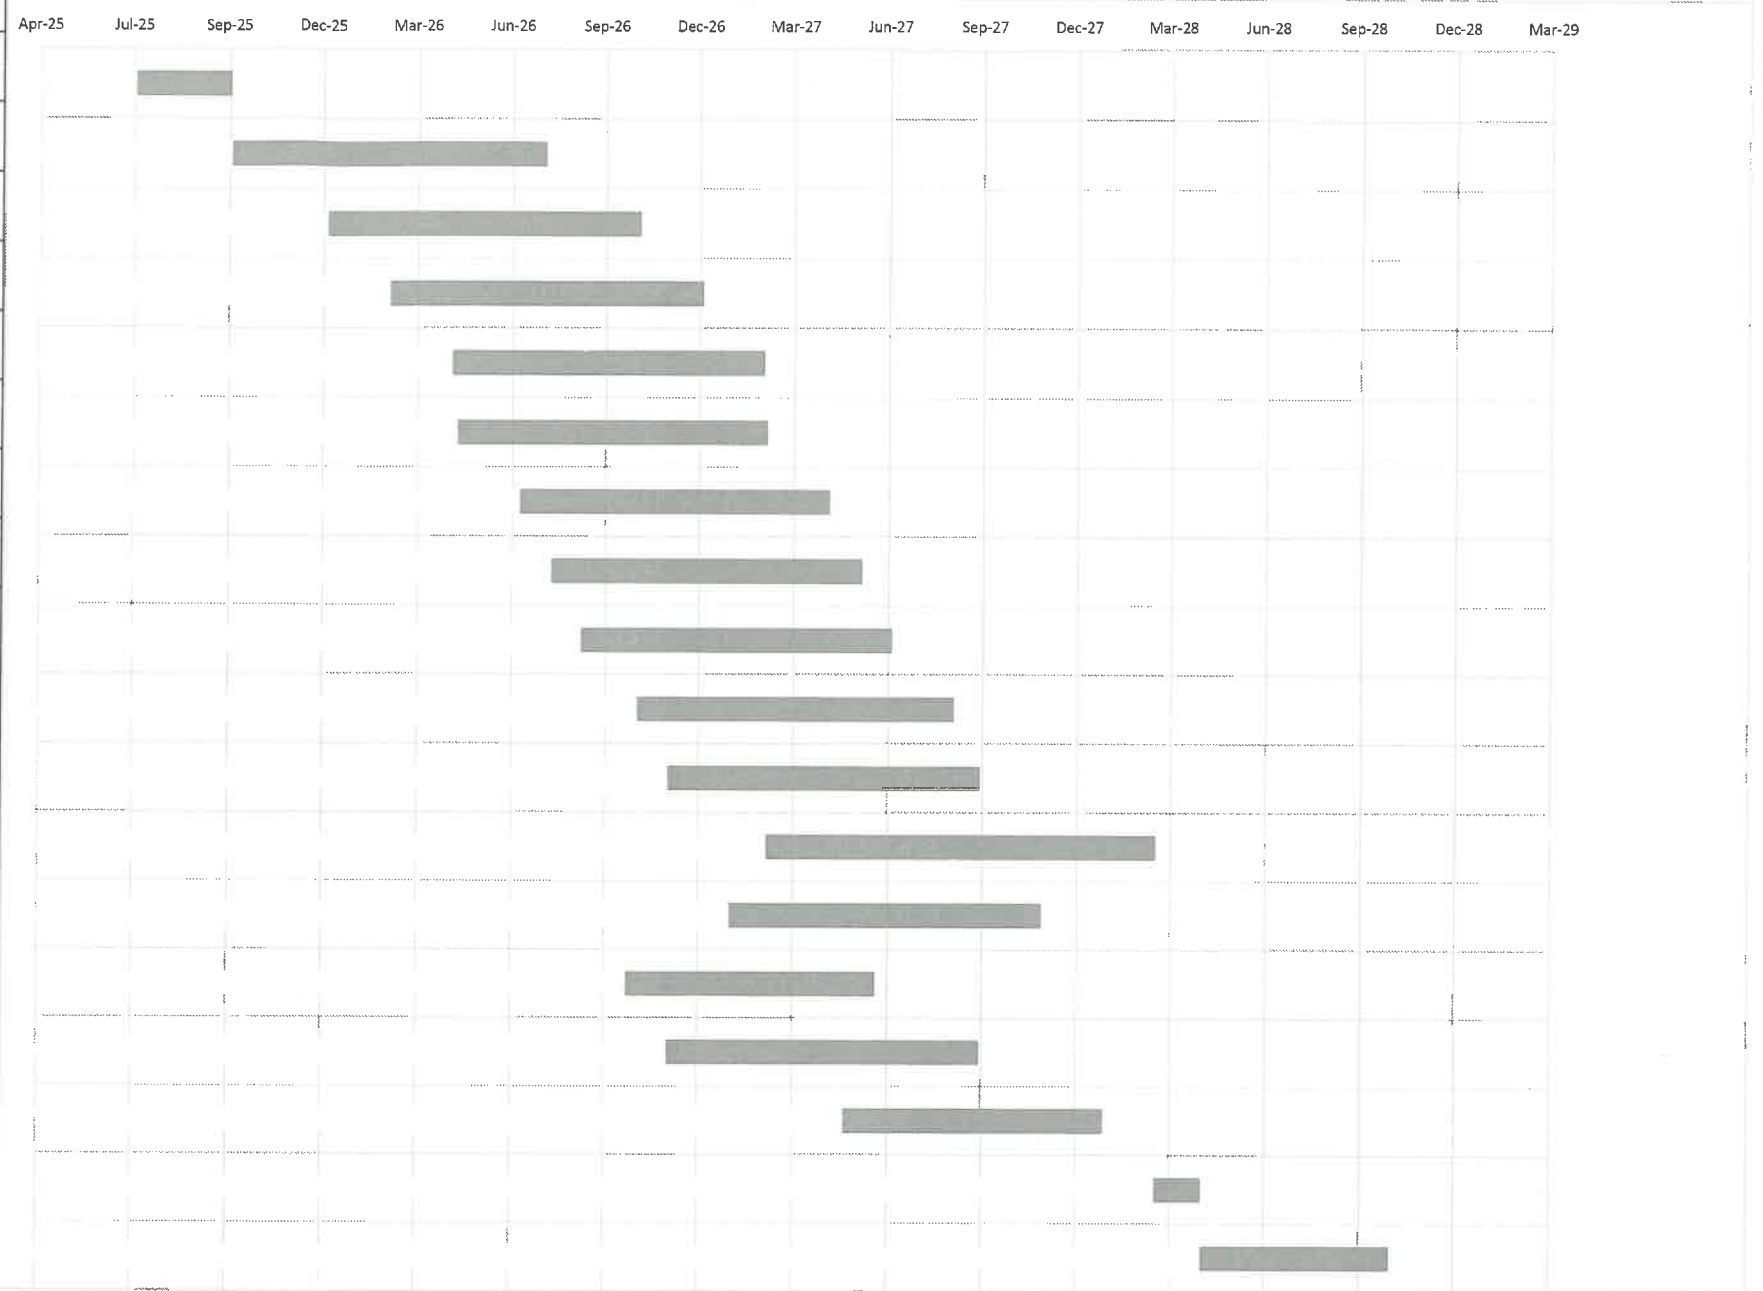

Handwritten signature and date:
28/10/24
